ID	Task Name	Duration	Start	Finish
1	**Kickoff meeting**	1 day	Wed 4/19/06	Wed 4/19/06
2	schedule recurring project meet	1 day	Thu 4/20/06	Thu 4/20/06
3	**Planning/Design**	**14 days**	**Wed 4/19/06**	**Mon 5/8/06**
4	Get GSB requirements	1 day	Wed 4/19/06	Wed 4/19/06
5	Review requirements	1 day	Thu 4/20/06	Thu 4/20/06
6	compile business requirem	2 days	Mon 4/24/06	Tue 4/25/06
7	Review GSB network	2 days	Wed 4/26/06	Thu 4/27/06
8	Gather statisitics on GSB r	2 days	Fri 4/28/06	Mon 5/1/06
9	Design/capacity planning	4 days	Tue 5/2/06	Fri 5/5/06
10	Design finalized	1 day	Mon 5/8/06	Mon 5/8/06
11	**Hardware**	**40 days**	**Mon 5/8/06**	**Fri 6/30/06**
12	Hardware requirements	1 day	Mon 5/8/06	Mon 5/8/06
13	determine cost/funding/buc	2 days	Tue 5/9/06	Wed 5/10/06
14	return eval form	1 day	Thu 5/11/06	Thu 5/11/06
15	Order equipment	1 day	Fri 5/12/06	Fri 5/12/06
16	Equipment arrives	8 days	Mon 5/15/06	Wed 5/24/06
17	Rack and stack equipment	2 days	Thu 5/25/06	Fri 5/26/06
18	Configure equipment	2 days	Mon 5/29/06	Tue 5/30/06
19	Order production units	2 days	Fri 6/9/06	Mon 6/12/06
20	Equipment arrives	10 days	Tue 6/13/06	Mon 6/26/06
21	rack and stack	1 day	Tue 6/27/06	Tue 6/27/06
22	configure	1 day	Wed 6/28/06	Wed 6/28/06
23	remove eval equipment	1 day	Thu 6/29/06	Thu 6/29/06
24	return eval equipment	1 day	Fri 6/30/06	Fri 6/30/06
25	**Test/Pilot**	**26 days**	**Mon 5/22/06**	**Mon 6/26/06**
26	Determine use/test cases I	3 days	Mon 5/22/06	Wed 5/24/06
27	Determine use/test cases f	3 days	Mon 5/22/06	Wed 5/24/06
28	Determine DR scenarios	1 day	Mon 5/22/06	Mon 5/22/06
29	setup configuration on test	2 days	Wed 5/31/06	Thu 6/1/06
30	Validate configuration	1 day	Fri 6/2/06	Fri 6/2/06
31	Test configuration	5 days	Mon 6/5/06	Fri 6/9/06
32	test monitoring	2 days	Mon 6/12/06	Tue 6/13/06

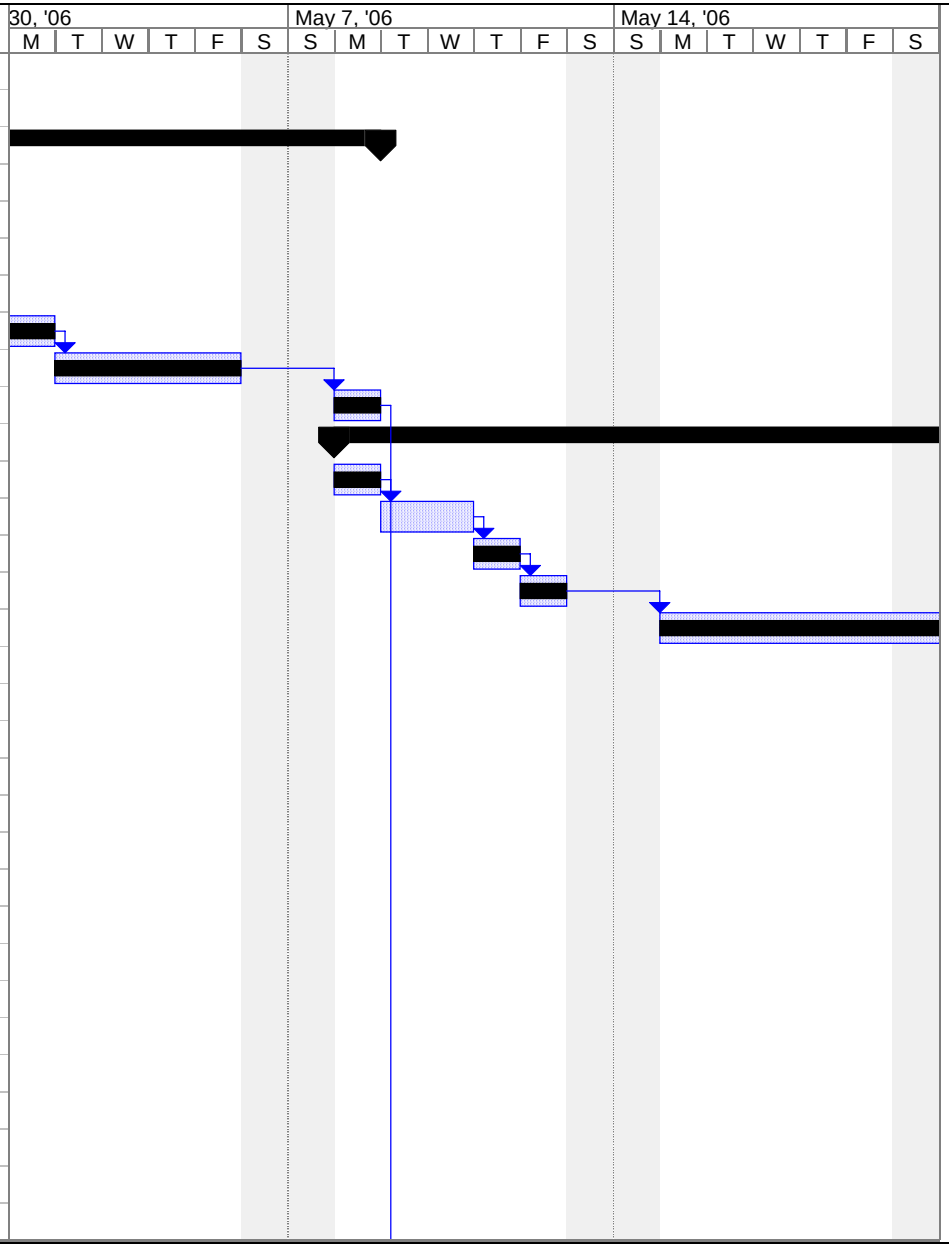

Project: Load balancer project4.mpp
Date: Tue 6/6/06

Task
Split
Progress
Milestone
Summary
Project Summary
External Tasks
External Milestone
Deadline

ID	Task Name	Duration	Start	Finish
33	GSB prepare applications a	2 days	Wed 6/14/06	Thu 6/15/06
34	GSB test use cases	4 days	Fri 6/16/06	Wed 6/21/06
35	DR tests	2 days	Thu 6/22/06	Fri 6/23/06
36	Go/no go	1 day	Mon 6/26/06	Mon 6/26/06
37	**Support**	**54 days**	**Wed 4/26/06**	**Mon 7/10/06**
38	Determine support model	1 day	Wed 4/26/06	Wed 4/26/06
39	identify support personel	1 day	Wed 4/26/06	Wed 4/26/06
40	identify training classes	1 day	Wed 4/26/06	Wed 4/26/06
41	book training classes	1 day	Fri 4/28/06	Fri 4/28/06
42	ITS Support training	5 days	Mon 6/26/06	Fri 6/30/06
43	GSB support training	2 days	Wed 7/5/06	Thu 7/6/06
44	Support handover from De	1 day	Fri 7/7/06	Fri 7/7/06
45	Live support	1 day	Mon 7/10/06	Mon 7/10/06
46	**Service Offering planning**	**66 days**	**Mon 4/24/06**	**Mon 7/24/06**
47	Get service offering info frc	5 days	Mon 4/24/06	Fri 4/28/06
48	review information	5 days	Mon 5/1/06	Fri 5/5/06
49	plan svc offering model	5 days	Mon 6/19/06	Fri 6/23/06
50	determine rates	5 days	Mon 6/26/06	Fri 6/30/06
51	svc offering signoff	1 day	Mon 7/3/06	Mon 7/3/06
52	Svc offering communicatio	5 days	Wed 7/5/06	Tue 7/11/06
53	Communication to campus	1 day	Mon 7/24/06	Mon 7/24/06
54	**Monitoring/Reporting**	**20 days**	**Mon 6/19/06**	**Fri 7/14/06**
55	Determine what to monitor	5 days	Mon 6/19/06	Fri 6/23/06
56	Determine monitoring meth	2 days	Mon 6/26/06	Tue 6/27/06
57	Design monitoring	5 days	Wed 6/28/06	Tue 7/4/06
58	Determine reporting needs	5 days	Wed 7/5/06	Tue 7/11/06
59	Create reports	3 days	Wed 7/12/06	Fri 7/14/06
60	**Documentation**	**39 days**	**Tue 5/9/06**	**Fri 6/30/06**
61	Design documentation con	3 days	Tue 5/9/06	Thu 5/11/06
62	Operational runbook comle	5 days	Mon 6/19/06	Fri 6/23/06
63	App owner runbook compl	5 days	Mon 6/26/06	Fri 6/30/06
64	**Implementation**	**13 days**	**Tue 7/11/06**	**Thu 7/27/06**

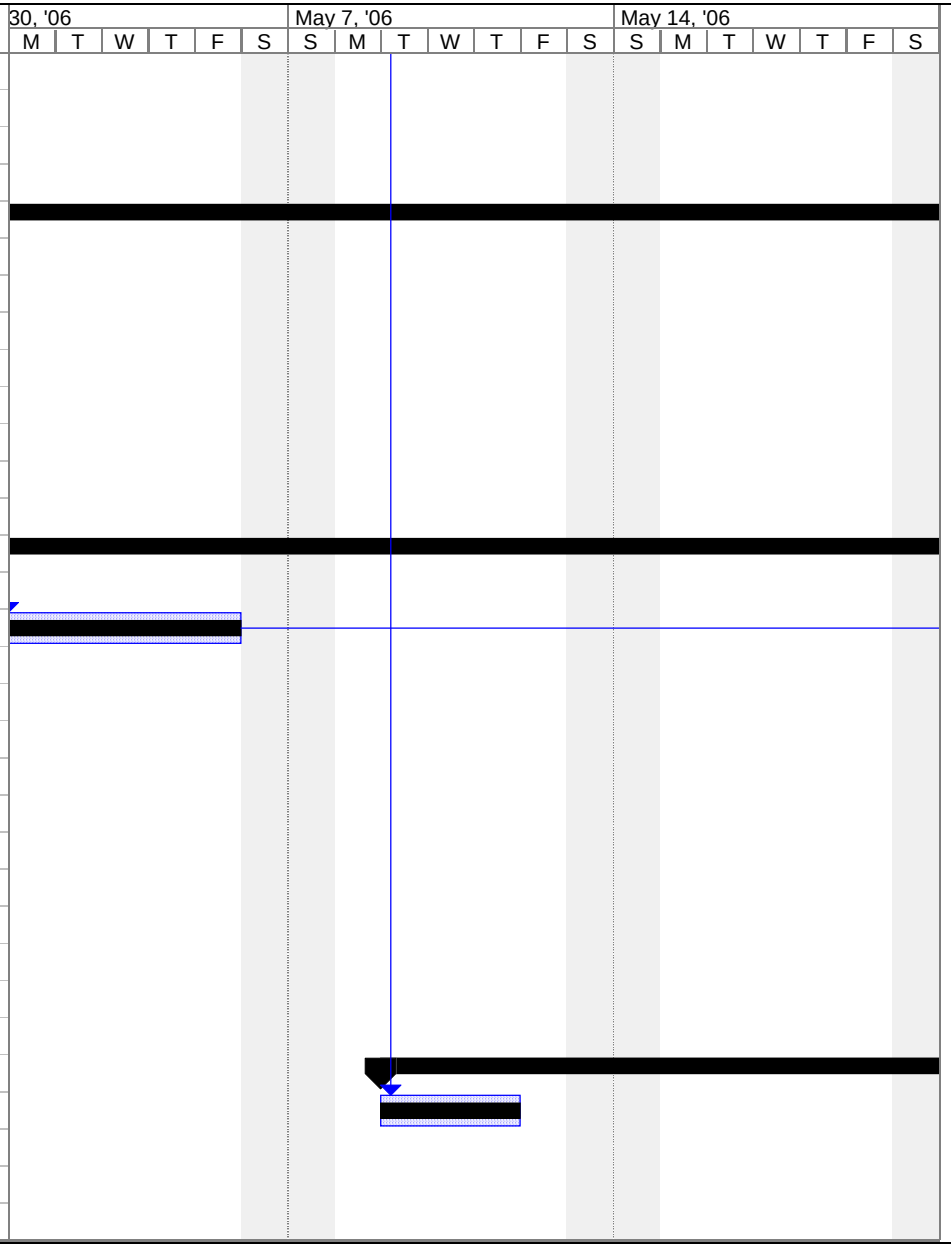

Project: Load balancer project4.mpp
Date: Tue 6/6/06

Task
Split
Progress
Milestone
Summary
Project Summary
External Tasks
External Milestone
Deadline
